



# QA Inspection Report

**Client:** FES FM

**Facility:** Dunbar Grammar

**Report Date:** 30/03/2018

**Roof Section:** New Build Roofs

## Report Data

Title	Main Extension
-------	----------------

Principal Contractor: FES Support Services Ltd

Roofing Contractor: Ronald Graham Roofing and Building Ltd

Waterproofing works are progressing well with the insulation and underlay now being installed. Approximately half of the flat area is now complete up to underlay and ready to receive the mineral capsheet.

Operatives will concentrate on encapsulating the perimeter parapet next week, once its been boarded out by others.

The felt works are being inspected for any loose laps and snagged as they go.

A further report will be issued next week.



**Photo 1**

Overview of insulation and underlay being installed.



**Photo 2**

Treated timber mechanically fixed to act as hard edge for flat board insulation and to create tapered gutter.




**Photo 3**

130mm PIR insulation boards mechanically fixed to vapour barrier.



**Photo 4**

Vented underlay torched to insulation.

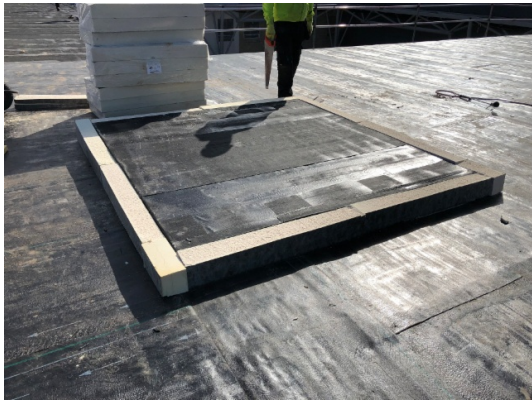

**Photo 5**

Change in level detail being insulated and waterproofed as per drawings.



**Photo 6**

Approximately half of the flat area is now complete up to underlay.
