

Client: East Lothian Council

Facility: 23 Newbigging

Report Date: 19/06/2014

Roof Section: Flat Roof

Report Data

Title	Final Inspection
-------	------------------

Contractor on site: Ronald Graham Roofing Ltd

Operatives on site: 6 ops

Weather Conditions: 16 degrees and sunny

Time of Inspection: 12.00pm

All roof sections are now fully installed to the residential block of flats. Garlands Stressply APP capsheet was used on the flat areas, with Garland Stressply Evo capsheet used at the upstands. We are happy with the quality of the completed roof, and now in a position to sign it off and issue the warranty.

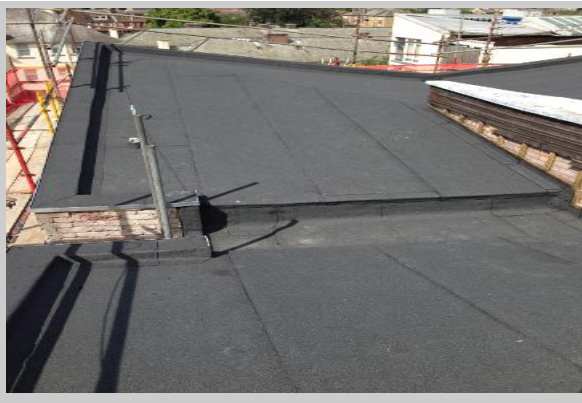


Photo 1
Overview of roof.



Photo 2
Completed roof section.



Photo 3

Neatly installed roof section.



Photo 4

Neat and tidy detailing work to the upstand.



Photo 5

Bitumen bleed out extruding from laps.

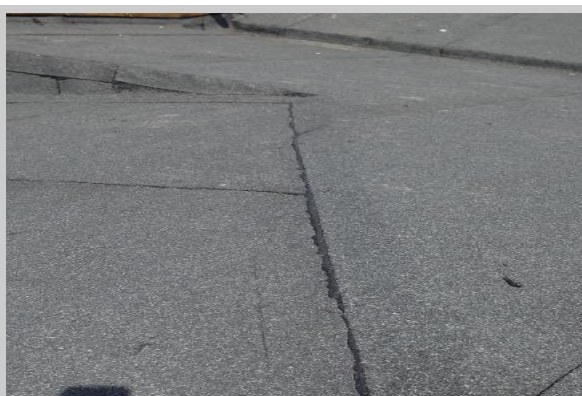


Photo 6

Good bleed out, ensuring the laps are well sealed.



Photo 7

Completed gutter detail.
